

IPRU PROJECT DASH BOARD

Last Updated:20-Apr-2016

47 sites are pending



No further Plan is possible beyond 26-Apr-16

Need focus of East site (on delivery & clearance)

Delay expected in UP & Halwani

Early completion of Agartala

Project Start Date	Count of working days	in %
28-Mar-16	19	
Total No. of Sites	140	
Site Clearance provided	93	66%
Completed	80	86%
Work In Progress		0%
Customer Issue	0	0%
Pending	13	14%
Site Clearance Awaited	47	34%

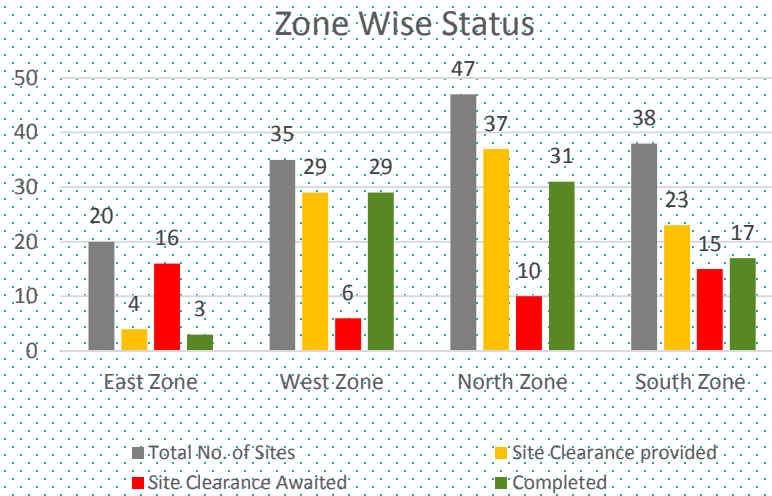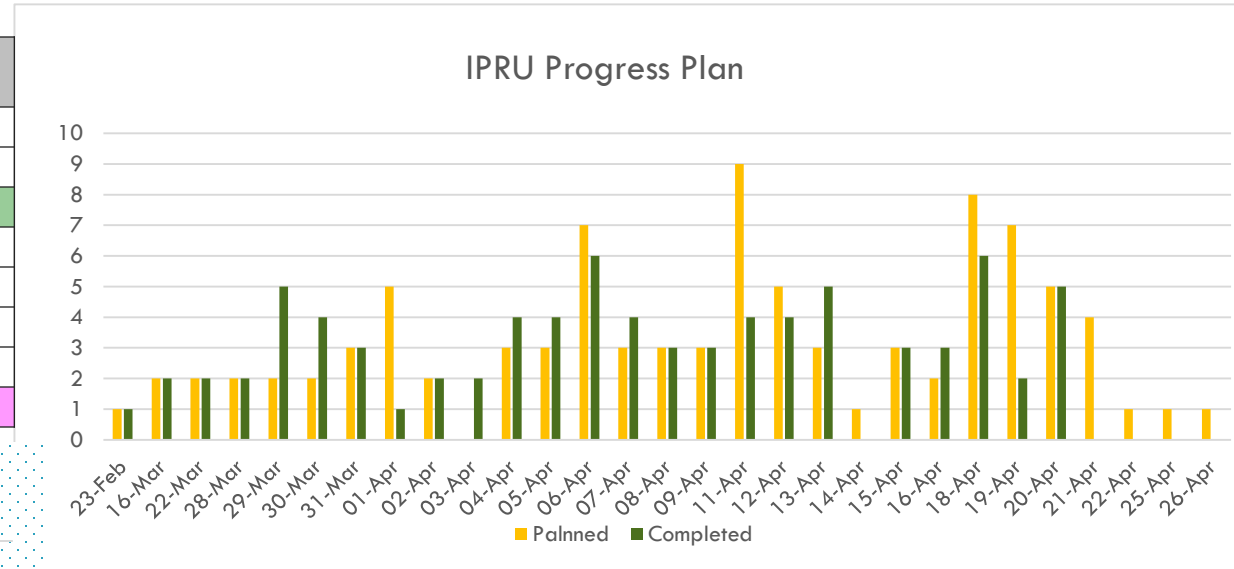

Pending Sites	
East	Balalore Berhampur Bhagalpur Bhubaneswar Cuttack Dhanbad Gorakhpur Imphal Jamshedpur Kolkata Muzaffarpur Patna Ranchi Raurkela Siliguri
South	Belgaum Chittor Guntur Kollam Kottayam Mangalore Palakkad Patthanamithitta Puducherry Rajahmudry Thiruviala Tirunelveli udupi Vijaywada Vizag
North	Agra Allahabad Banswara Bhatinda Derhadun Jabaplpur Jammu Kota
West	Anand Goa Jamnagar Mumbai Rajkot Ratlam

